

Class: AIML 5D
SRN: PES1UG24AM200
Name: Pratham S Reddy

SOFTWARE ENGINEERING LAB 2

Agile Project Planning and Sprint Simulation using Jira

Academic Elective Bidding & Allocation System

Project Key: SCRUM

Sprints: SCRUM Sprint 1 and SCRUM Sprint 2

1. Project Overview

The Academic Elective Bidding & Allocation System is organised in Jira using Agile Scrum. The project breaks the overall system into Epics and User Stories, assigns story points and priorities, and then tracks implementation through two sprints. The evidence in this report follows the same practical sequence used in the Jira workspace: project structure, backlog and stories, sprint execution, comments/review, progress tracking, burndown charts and sprint completion.

Project Item	Details
Jira Project	Academic Elective Bidding & Allocation System
Project Key	SCRUM
Method	Agile Scrum
Sprints	SCRUM Sprint 1 and SCRUM Sprint 2
Sprint 1 Goal	Complete the student access and bidding credit foundation for the elective bidding system.
Sprint 2 Goal	Complete elective bidding, allocation, validation, conflict handling and result publication.

2. Epics

The Jira project is divided into six functional Epics. Two Epics are addressed in Sprint 1 and four are addressed in Sprint 2. This separation keeps the early student-facing foundation independent from the later bidding, allocation and administration workflow.

Epic Key	Epic	Sprint Focus
SCRUM-11	Student Access & Elective Discovery	Sprint 1
SCRUM-12	Bidding Credit Management	Sprint 1
SCRUM-13	Elective Bid Submission & Management	Sprint 2
SCRUM-14	Elective Allocation	Sprint 2
SCRUM-15	Academic Administration & Results	Sprint 2
SCRUM-16	Validation & Conflict Management	Sprint 2

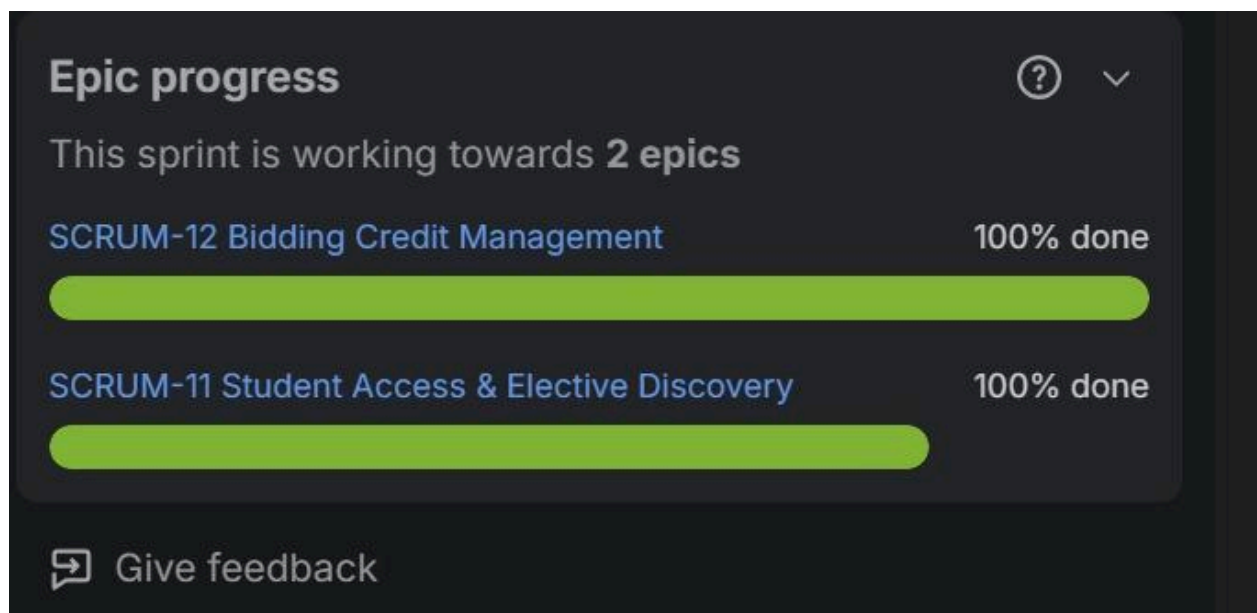


Figure 1. Sprint 1 Epic Progress — Student Access & Elective Discovery and Bidding Credit Management are shown as 100% complete.

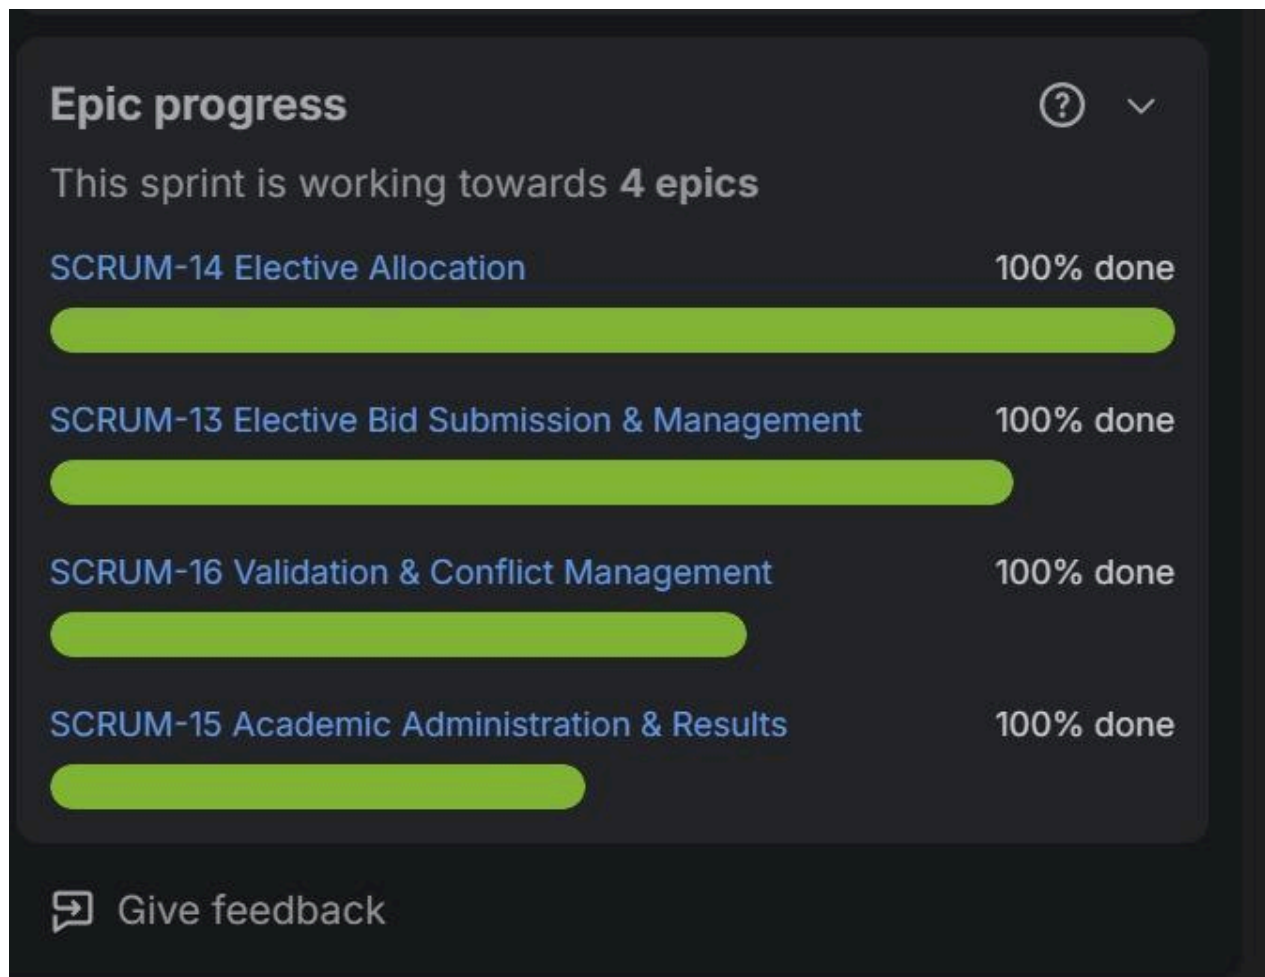


Figure 2. Sprint 2 Epic Progress — four Epics are shown as 100% complete: Elective Allocation, Elective Bid Submission & Management, Validation & Conflict Management, and Academic Administration & Results.

3. Epic and User Story Table

The following master table is the main planning table for this project. It combines the Epic, Epic Key, User Story, Issue Key, Story Points, Priority and Sprint columns so that the complete Jira backlog can be understood in one place.

Epic	Epic Key	User Story	Issue Key	Story Points	Priority	Sprint
Student Access & Elective Discovery	SCRUM-11	Student Login	SCRUM-17	2	Highest	Sprint 1
Student Access & Elective Discovery	SCRUM-11	View Available Electives	SCRUM-19	3	Highest	Sprint 1
Student Access & Elective Discovery	SCRUM-11	Check Prerequisites	SCRUM-20	3	High	Sprint 1
Bidding Credit Management	SCRUM-12	View Bidding Credits	SCRUM-21	2	High	Sprint 1
Bidding Credit Management	SCRUM-12	Allocate Bidding Credits	SCRUM-22	5	Highest	Sprint 1
Bidding Credit Management	SCRUM-12	Check Credit Limit	SCRUM-23	3	High	Sprint 1
Elective Bid Submission & Management	SCRUM-13	Submit Elective Bids	SCRUM-24	8	Highest	Sprint 2

Epic	Epic Key	User Story	Issue Key	Story Points	Priority	Sprint
Elective Bid Submission & Management	SCRUM-13	Validate Bids	SCRUM-25	5	Highest	Sprint 2
Elective Bid Submission & Management	SCRUM-13	Modify Bids	SCRUM-26	5	Highest	Sprint 2
Elective Allocation	SCRUM-14	Configure Bidding	SCRUM-27	5	Medium	Sprint 2
Elective Allocation	SCRUM-14	Run Elective Allocation	SCRUM-28	8	High	Sprint 2
Validation & Conflict Management	SCRUM-16	Check Timetable Conflicts	SCRUM-33	5	Medium	Sprint 2
Elective Allocation	SCRUM-14	Resolve Allocation Conflicts	SCRUM-29	8	Medium	Sprint 2
Validation & Conflict Management	SCRUM-16	Allocation Constraint Validation	SCRUM-34	8	Medium	Sprint 2
Academic Administration & Results	SCRUM-15	Manage Elective Courses	SCRUM-30	5	Medium	Sprint 2
Academic Administration & Results	SCRUM-15	Publish Allocation Results	SCRUM-31	3	Medium	Sprint 2
Academic Administration & Results	SCRUM-15	View Allocation Result	SCRUM-32	2	Medium	Sprint 2

4. User Story Evidence

The backlog screenshots provide direct evidence of the stories, their issue keys, epic association, story-point estimates and priority indicators.

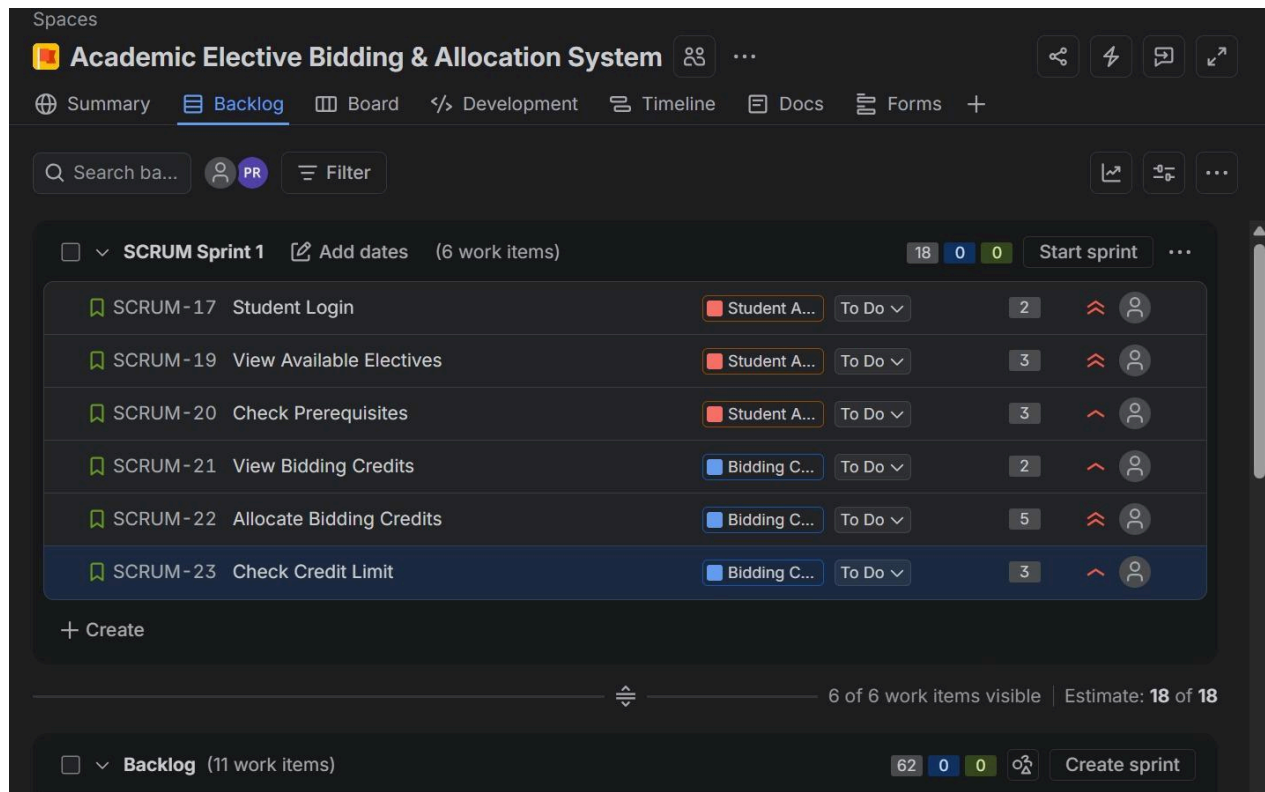


Figure 3. Sprint 1 backlog — six committed User Stories with a total estimate of 18 story points.

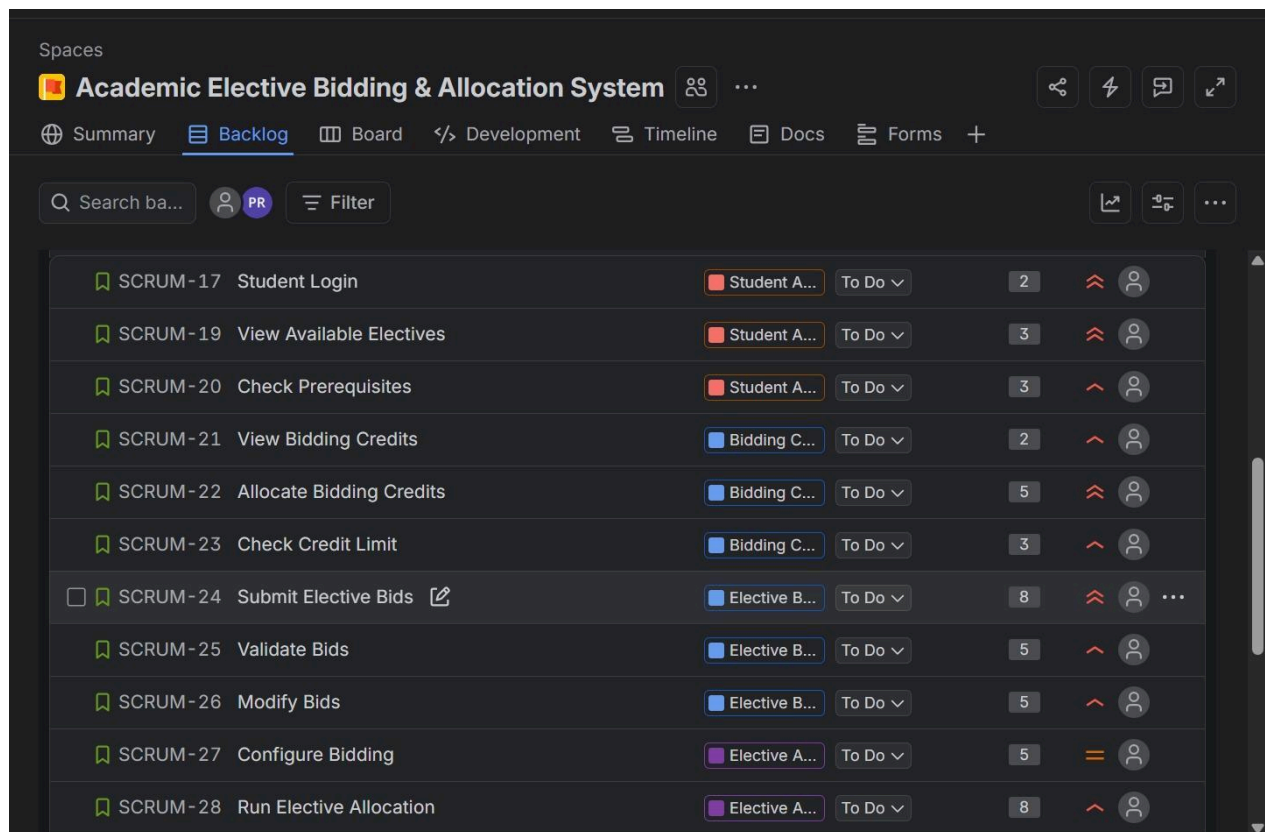


Figure 4. Main backlog view — Sprint 1 stories followed by Sprint 2 stories, including their story-point estimates and priority indicators.

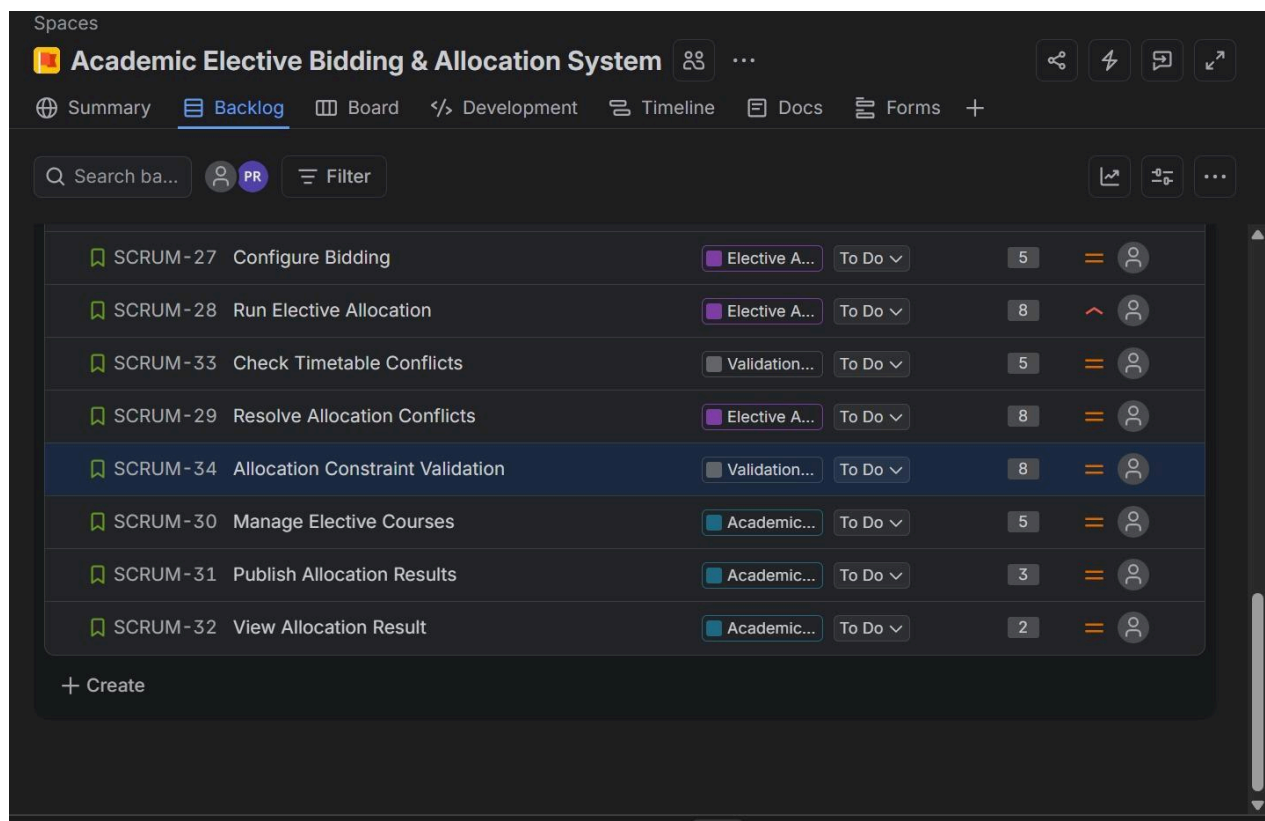


Figure 5. Sprint 2 backlog continuation — allocation, validation and result-related User Stories with their story-point estimates.

The individual story evidence and workflow screenshots are included below as part of the sprint execution record.

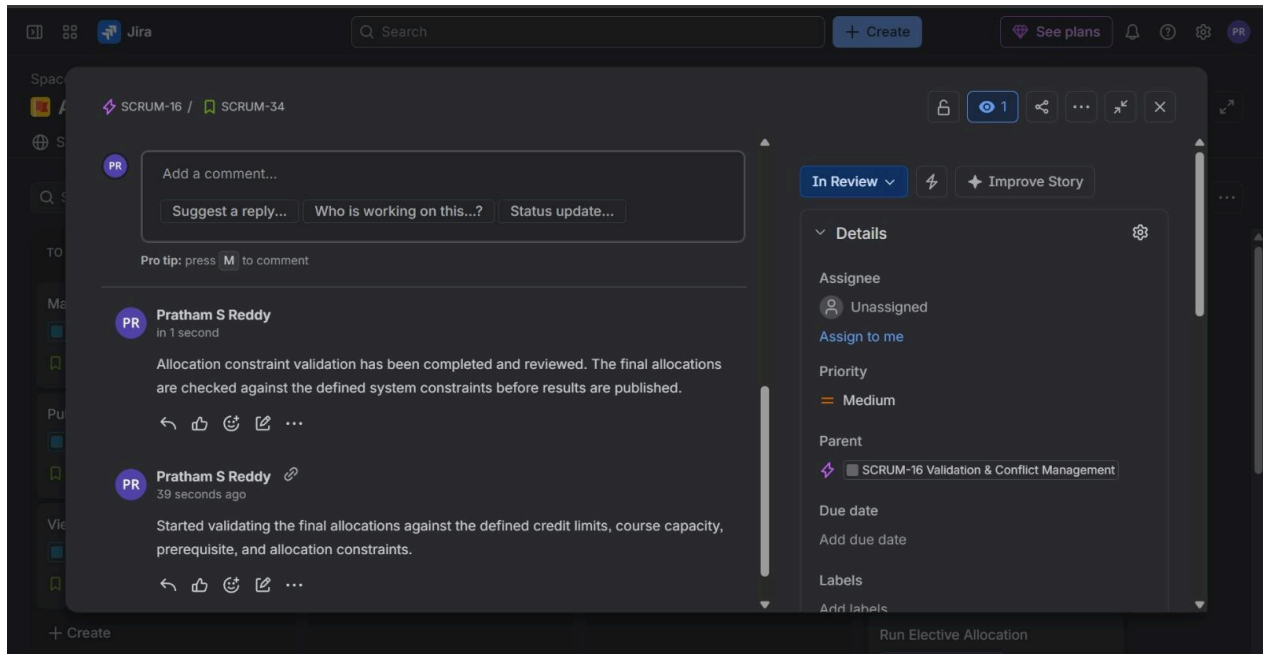


Figure 6. Individual User Story evidence and activity/comments view for Allocation Constraint Validation (SCRUM-34).

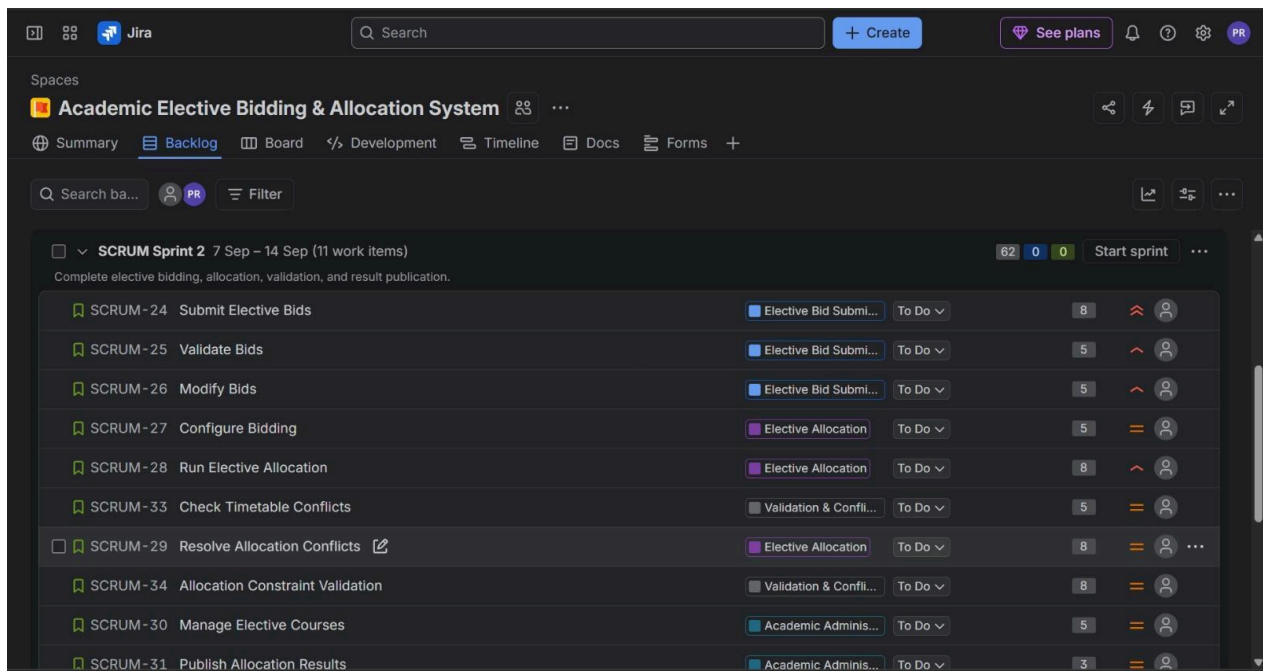


Figure 7. Jira backlog/list view showing the complete set of project work items and their organisation.

5. Priority and Story-Point Planning

Story points represent relative effort and complexity rather than hours. The project uses a small Fibonacci-style set of values visible in the Jira backlog. Priority indicators are used to bring more important functionality forward in the backlog.

Sprint	Committed Stories	Story Points
Sprint 1	6	18
Sprint 2	11	62
Total	17	80

The Sprint 1 backlog screenshot explicitly shows six work items and an estimate of 18 story points. The Sprint 2 backlog is shown as 11 work items with an estimate of 62 story points. These figures are also reflected in the sprint progress and burndown evidence.

Start Sprint

×

6 work items will be included in this sprint.

Required fields are marked with an asterisk *

Sprint name *

SCRUM Sprint 1

Duration *

1 week

Start date *

8/31/2026 11:42 AM

Planned start date: 8/31/2026, 11:30 AM
A sprint's start date impacts velocity and scope in reports. [Learn more.](#)
Date format: MM/DD/YYYY. Time format: e.g. 1:00 PM.

End date *

9/7/2026 11:30 AM

☒ Automatically complete sprint

Sprint goal

Complete the student access and bidding credit foundation for the elective bidding system.

CancelStart

Figure 8. Sprint 2 start-sprint setup screen, showing the sprint configuration before execution.




Figure 9. Sprint 1 completion dialog, confirming that the sprint contained six completed work items.

6. Comments and Review Activity

Jira comments are used as lightweight evidence of work progression. They record what was checked, what was completed and when an item was ready for review. The project also uses the In Review workflow state before final completion.

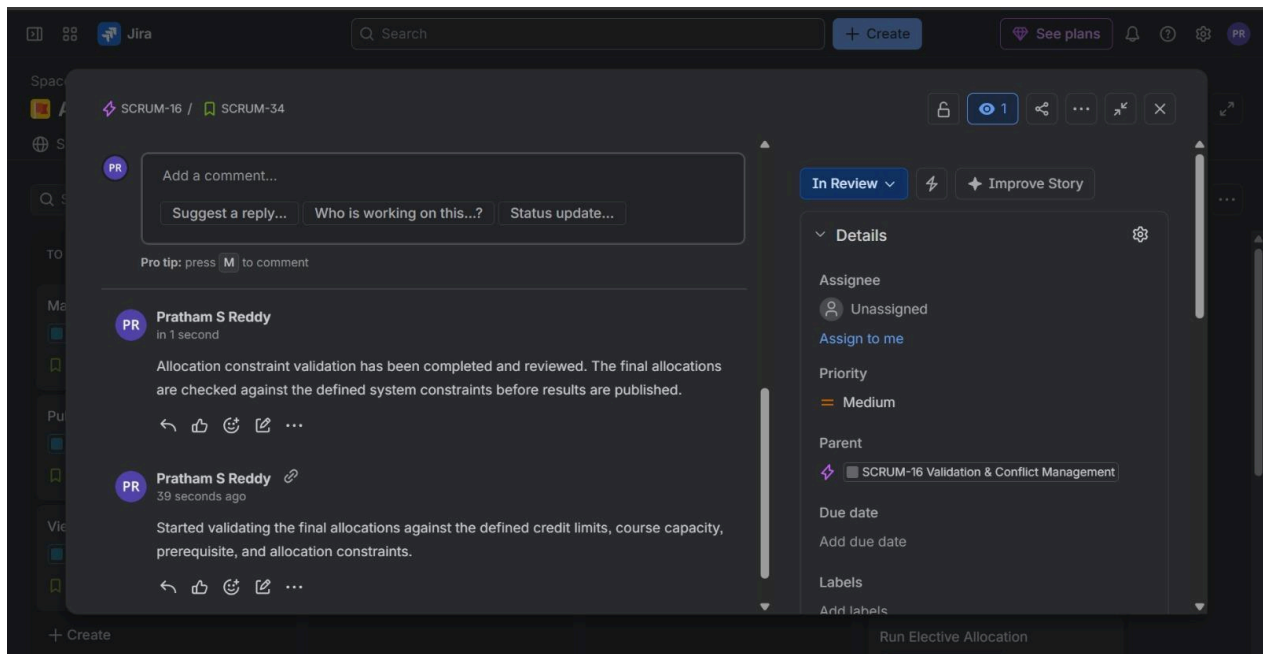


Figure 10. Review/activity evidence on the Allocation Constraint Validation story, showing progress comments and issue activity.

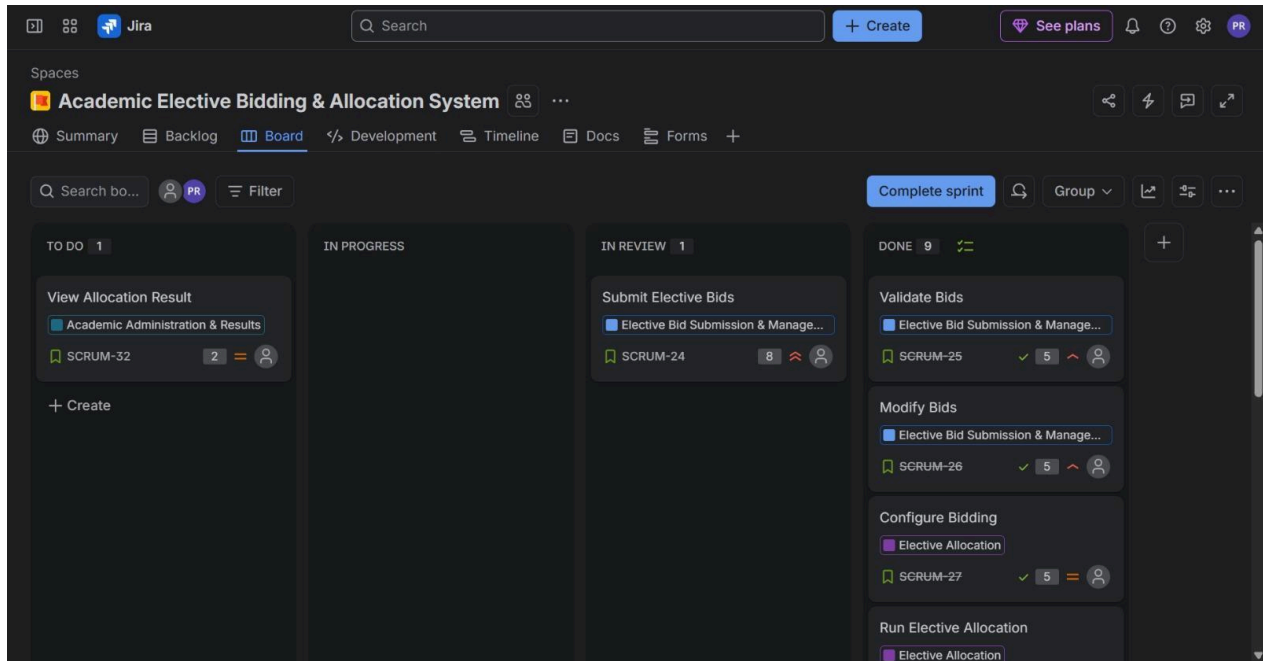


Figure 11. Sprint board state showing a work item positioned for review while the remaining project work is tracked in the board.

For the report, the comment evidence is treated separately from the board screenshots so that the reviewer can see both the workflow state and the supporting activity record.

7. Sprint 1

7.1 Sprint 1 Scope

Sprint 1 establishes the foundation of the elective bidding system. It concentrates on student access, elective discovery, prerequisite checking and management of bidding credits.

User Story	Issue Key	Points	Epic
Student Login	SCRUM-17	2	Student Access & Elective Discovery
View Available Electives	SCRUM-19	3	Student Access & Elective Discovery
Check Prerequisites	SCRUM-20	3	Student Access & Elective Discovery
View Bidding Credits	SCRUM-21	2	Bidding Credit Management
Allocate Bidding Credits	SCRUM-22	5	Bidding Credit Management
Check Credit Limit	SCRUM-23	3	Bidding Credit Management
Total		18	

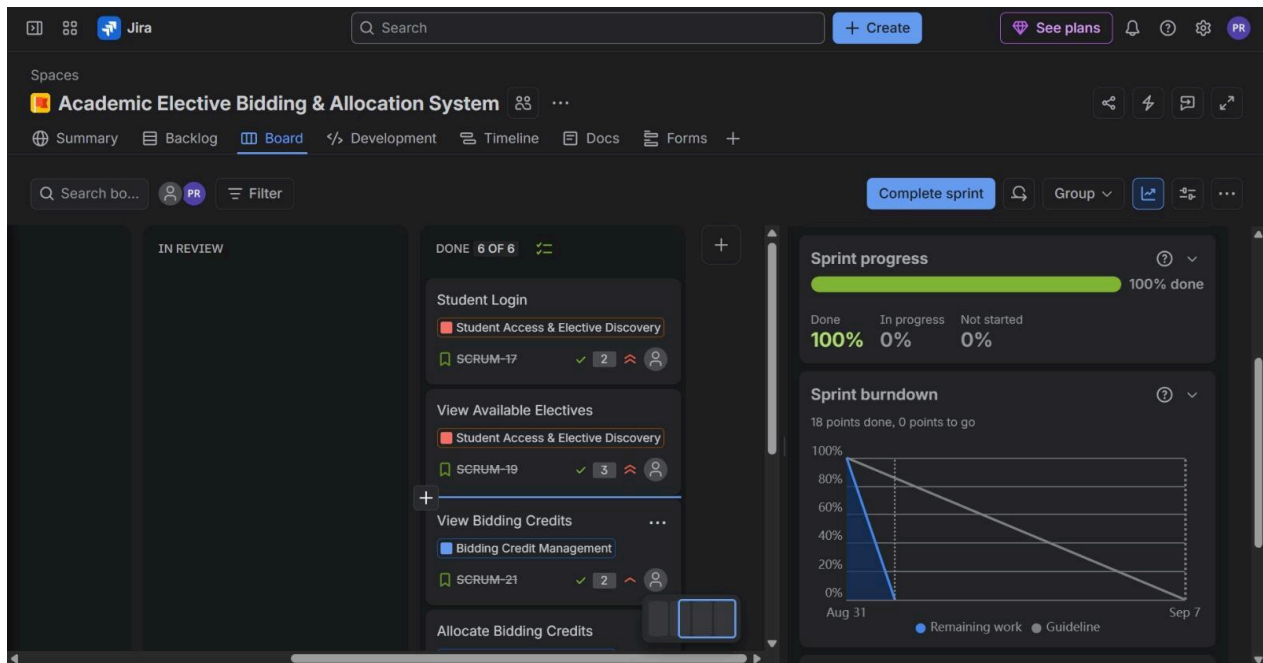
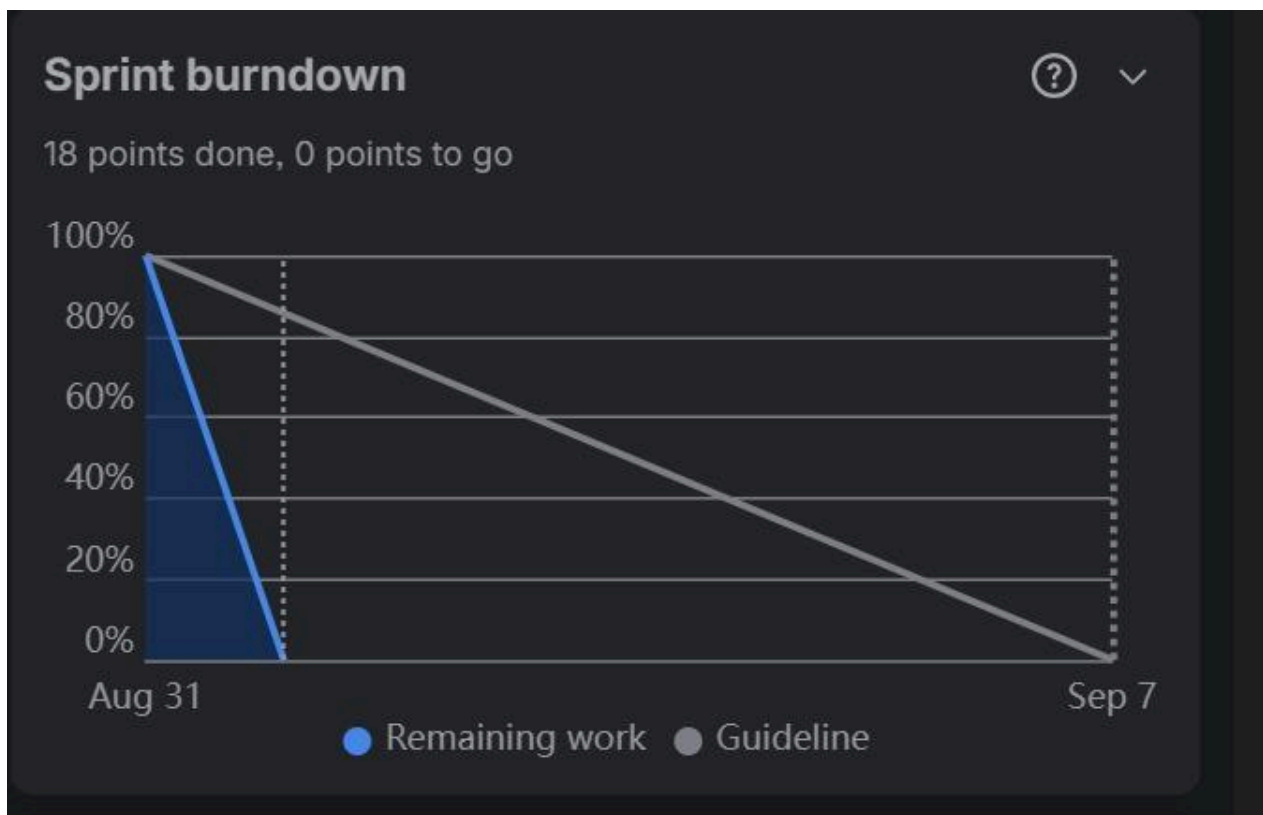


Figure 12. Sprint 1 board during execution, showing stories moving through the Scrum workflow and the sprint insights panel.



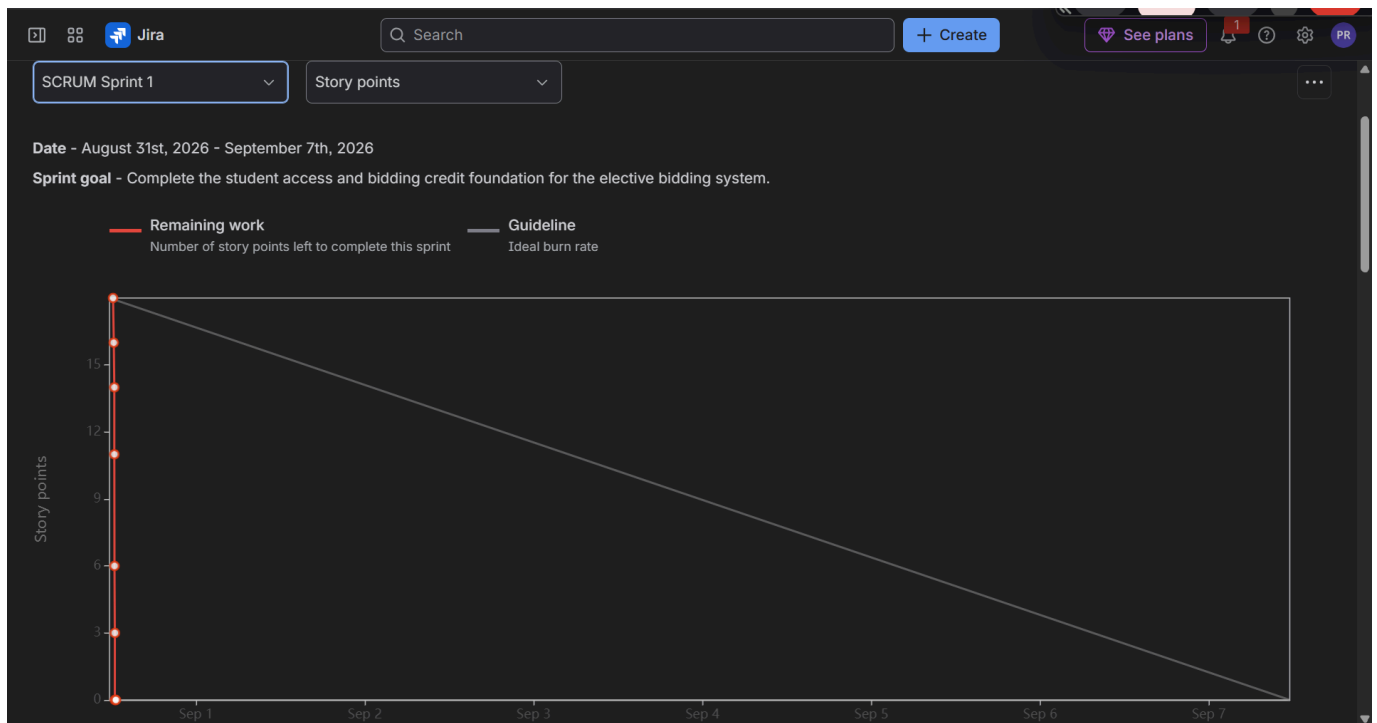


Figure 13. Sprint 1 burndown chart — 18 story points are shown as completed and 0 points remain.

7.2 Sprint 1 Progress

The Sprint 1 progress evidence shows the work being tracked through Jira's To Do, In Progress, In Review and Done columns. The sprint insights panel reports 100% completion, with no work left in progress or not started at the final state.

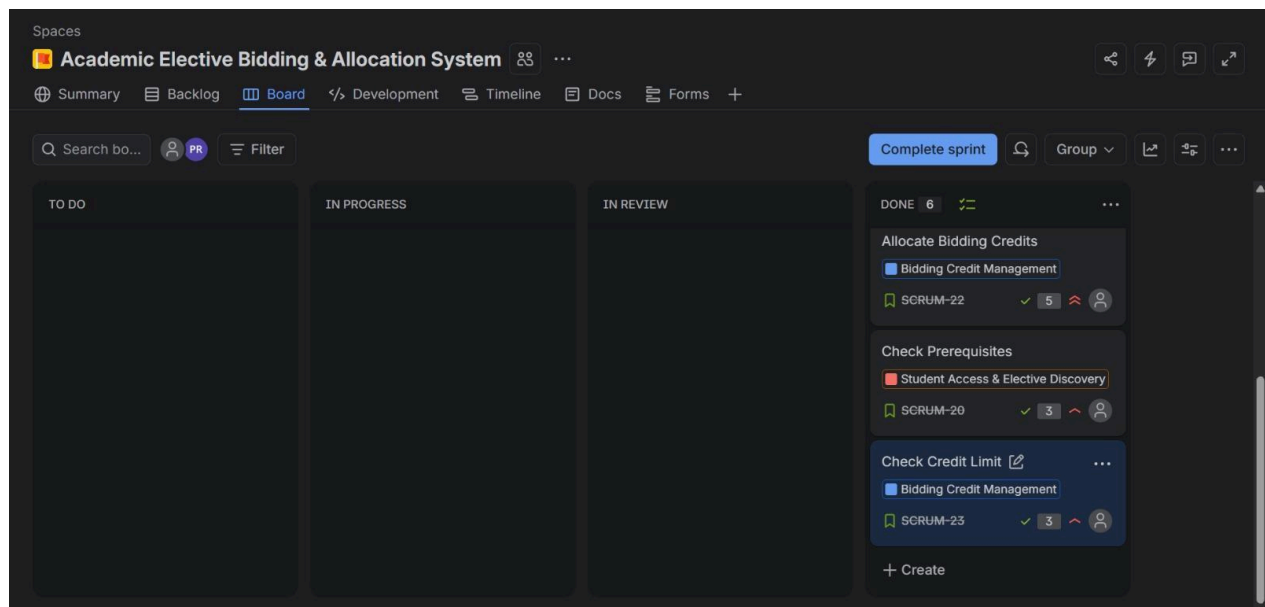


Figure 14. Sprint 1 board state during execution, showing the distribution of stories across the workflow.

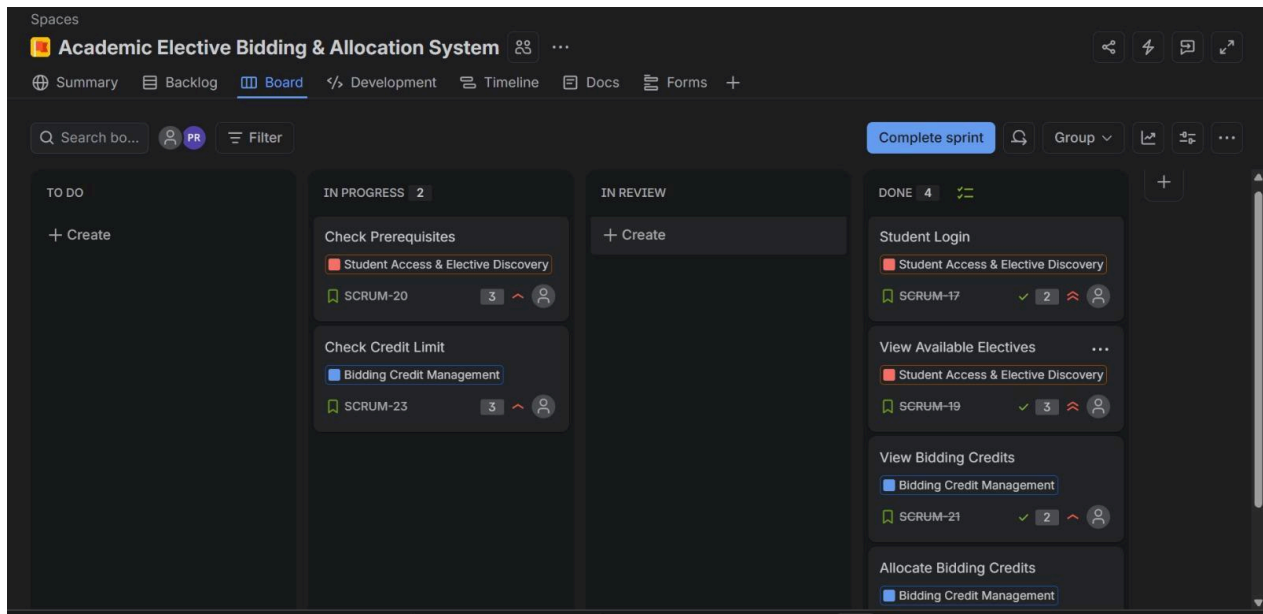


Figure 15. Sprint 1 board state showing further movement of committed stories toward completion.

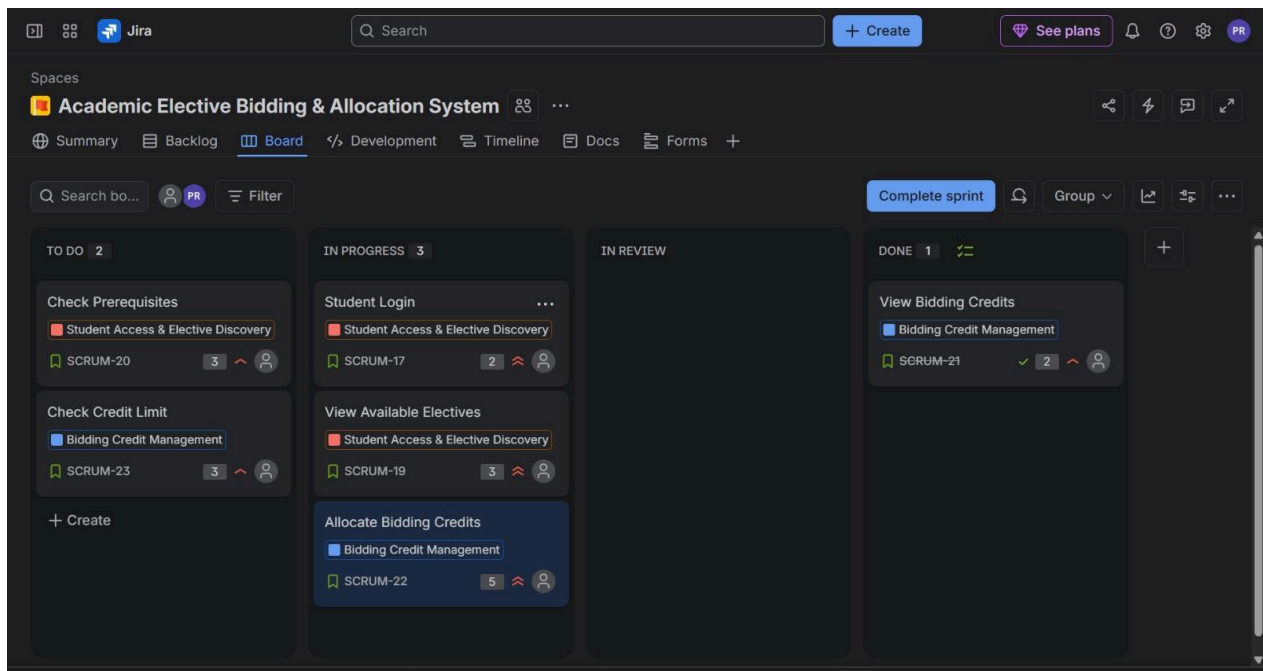


Figure 16. Sprint 1 board state with completed work concentrated in the Done column.

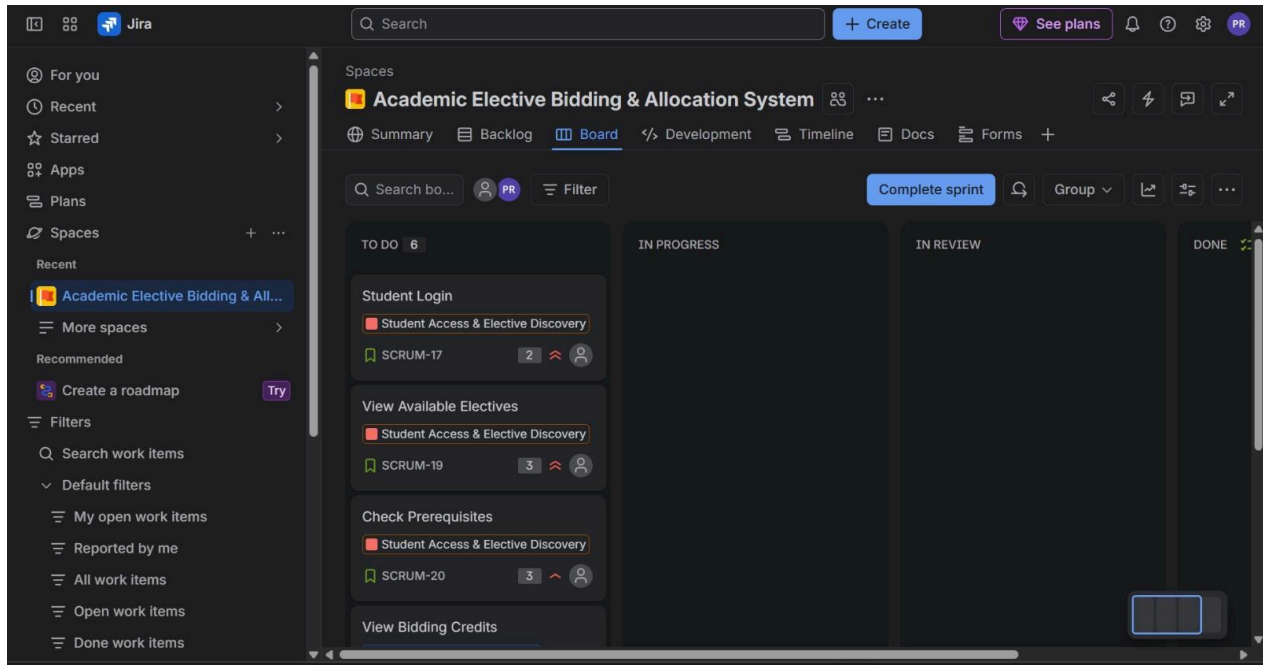


Figure 17. Sprint 1 later board state, showing the final workflow arrangement before sprint closure.

8. Sprint 2

8.1 Sprint 2 Scope

Sprint 2 completes the main bidding and allocation pipeline. Its work covers bid submission and modification, allocation configuration and execution, timetable and constraint validation, conflict resolution, elective administration and publication/viewing of allocation results.

User Story	Issue Key	Points	Epic
Submit Elective Bids	SCRUM-24	8	Elective Bid Submission & Management
Validate Bids	SCRUM-25	5	Elective Bid Submission & Management
Modify Bids	SCRUM-26	5	Elective Bid Submission & Management
Configure Bidding	SCRUM-27	5	Elective Allocation
Run Elective Allocation	SCRUM-28	8	Elective Allocation
Check Timetable Conflicts	SCRUM-33	5	Validation & Conflict Management
Resolve Allocation Conflicts	SCRUM-29	8	Elective Allocation
Allocation Constraint Validation	SCRUM-34	8	Validation & Conflict Management
Manage Elective Courses	SCRUM-30	5	Academic Administration & Results
Publish Allocation Results	SCRUM-31	3	Academic Administration & Results
View Allocation Result	SCRUM-32	2	Academic Administration & Results
Total		62	

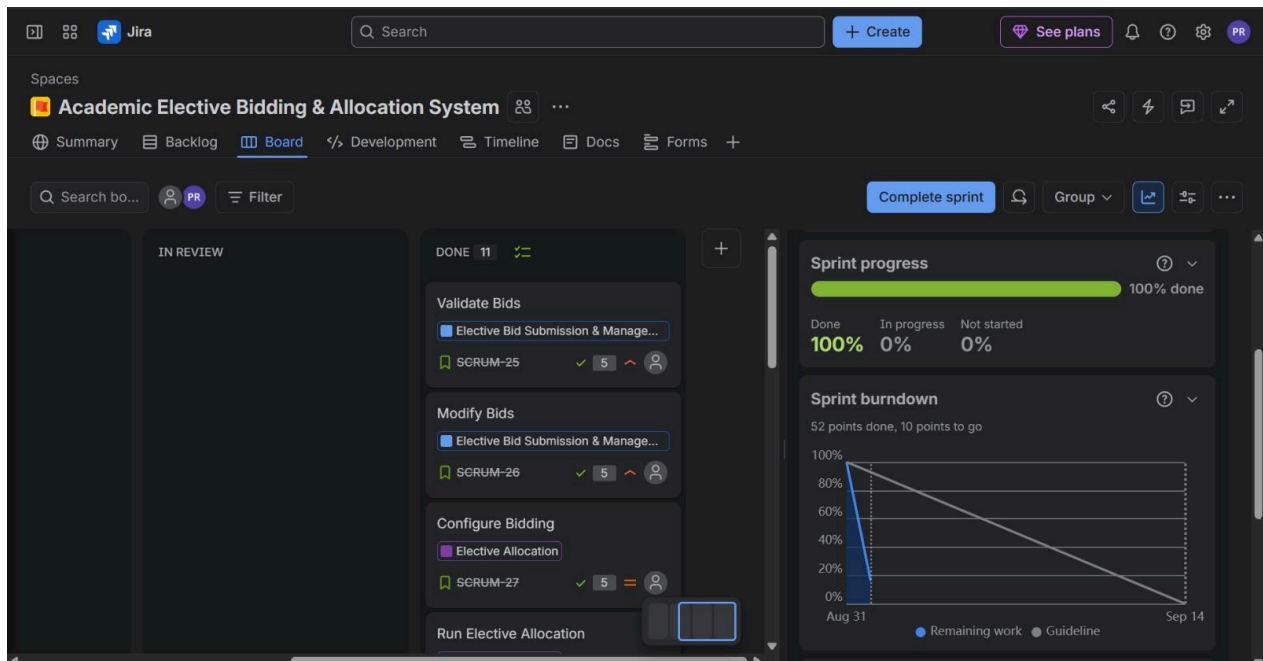


Figure 18. Sprint 2 board with sprint progress and burndown tracking visible.

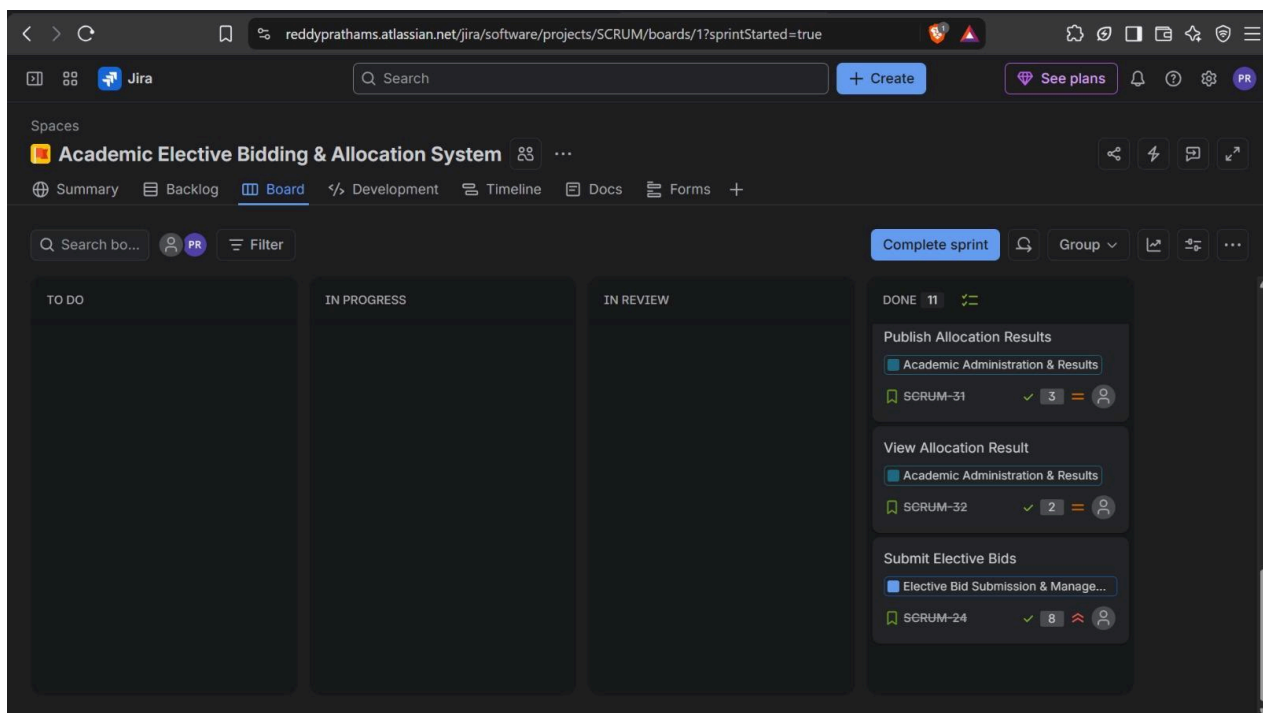


Figure 19. Sprint 2 board state showing the completed and remaining work distribution.

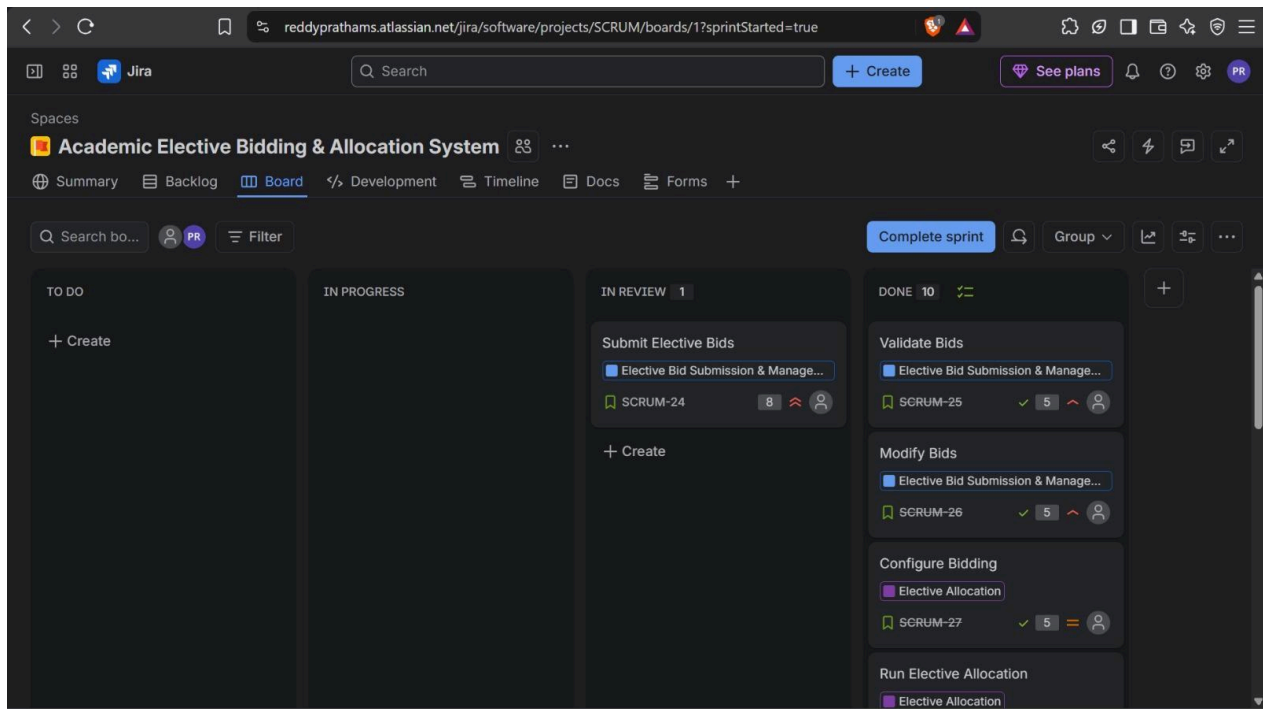


Figure 20. Sprint 2 board state as the workflow progresses toward completion.

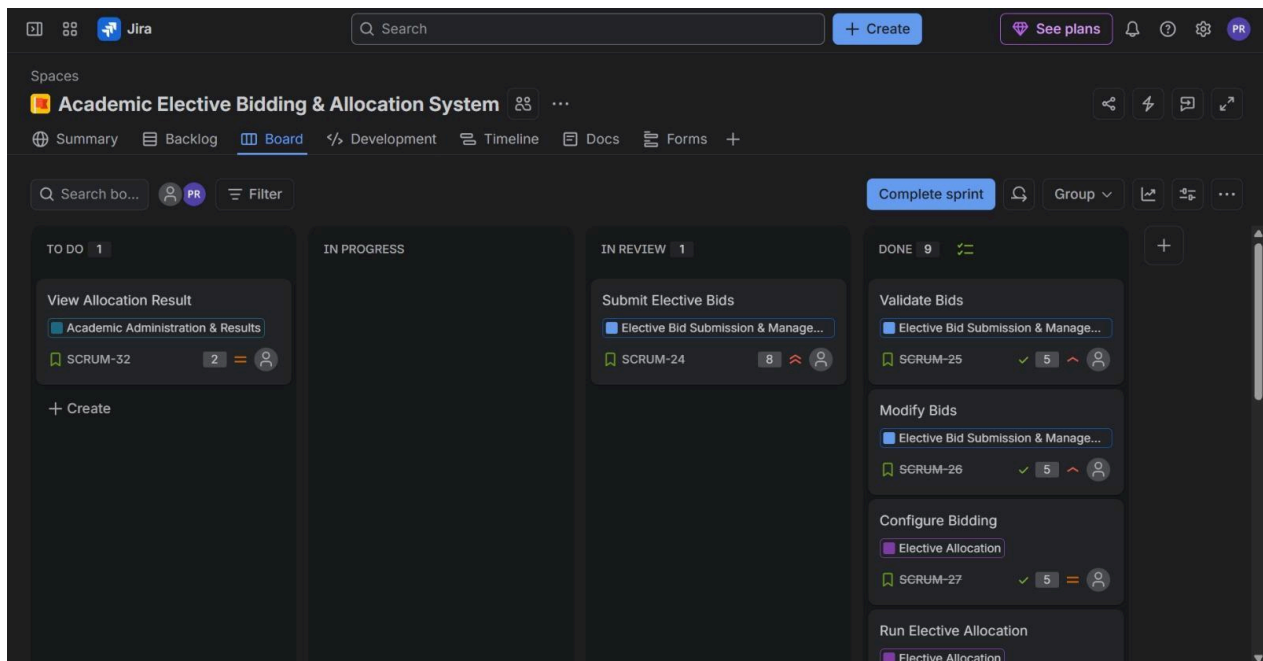


Figure 21. Sprint 2 board state showing allocation and validation work moving through the workflow.

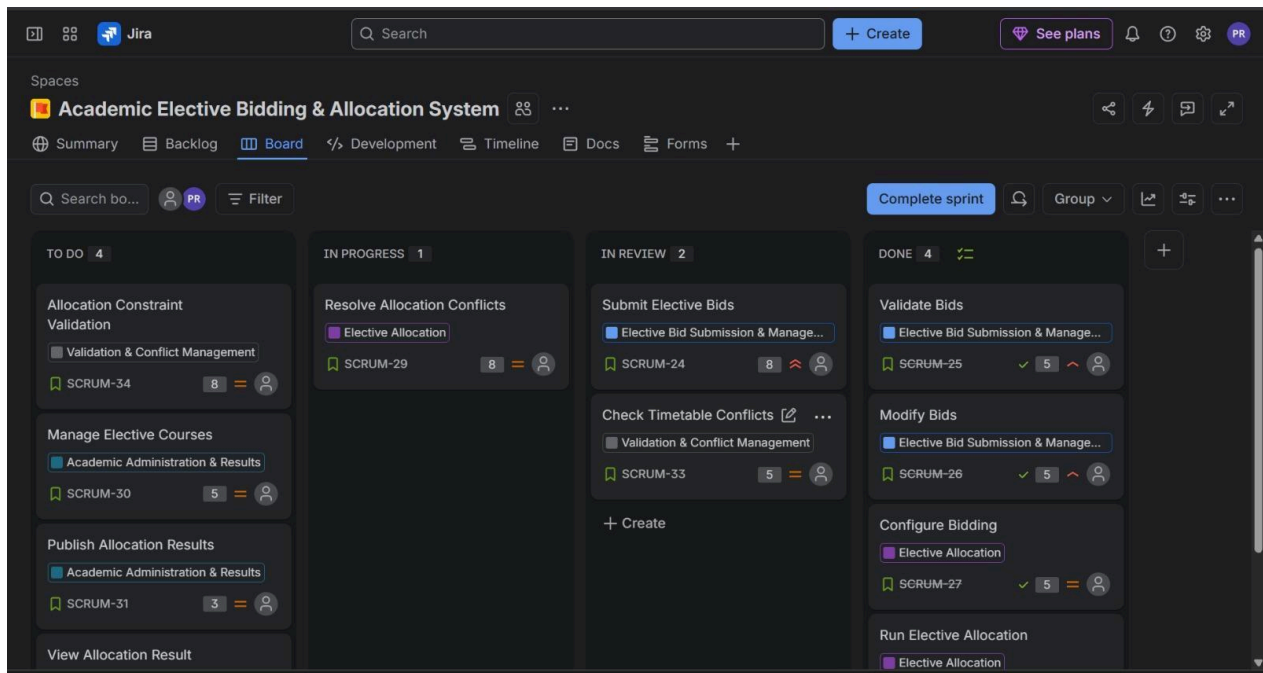


Figure 22. Sprint 2 board state with additional stories moved toward completion.

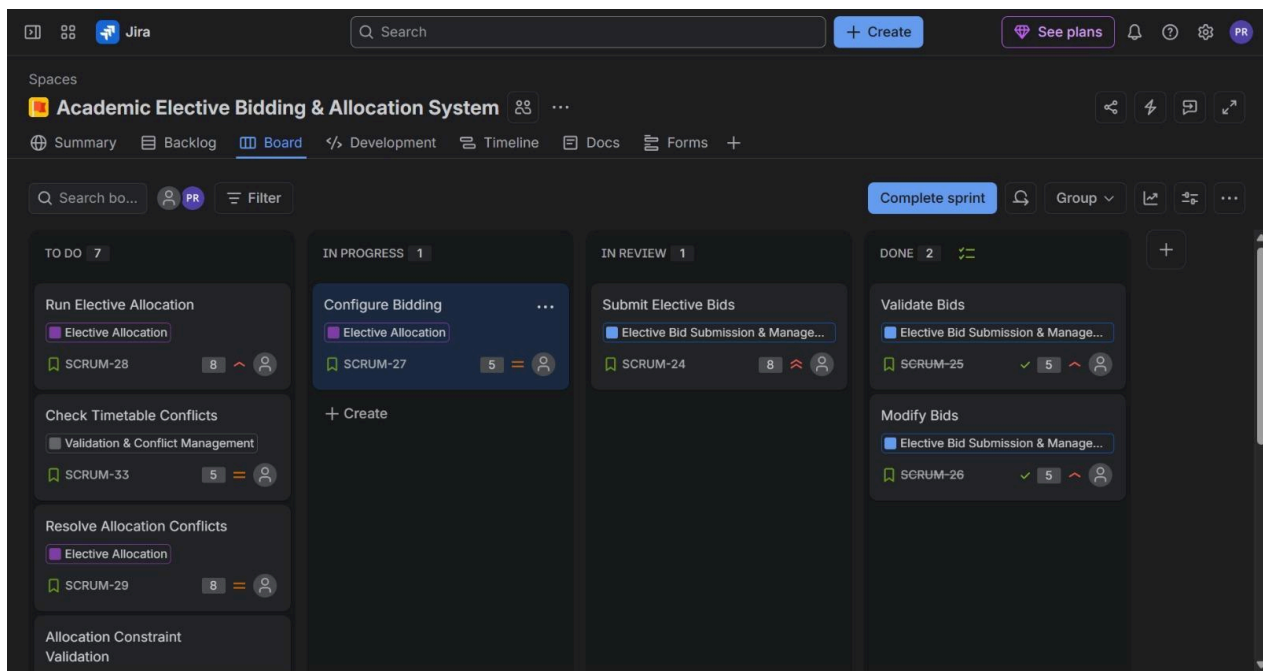


Figure 23. Sprint 2 board state showing continued progress across the Scrum columns.

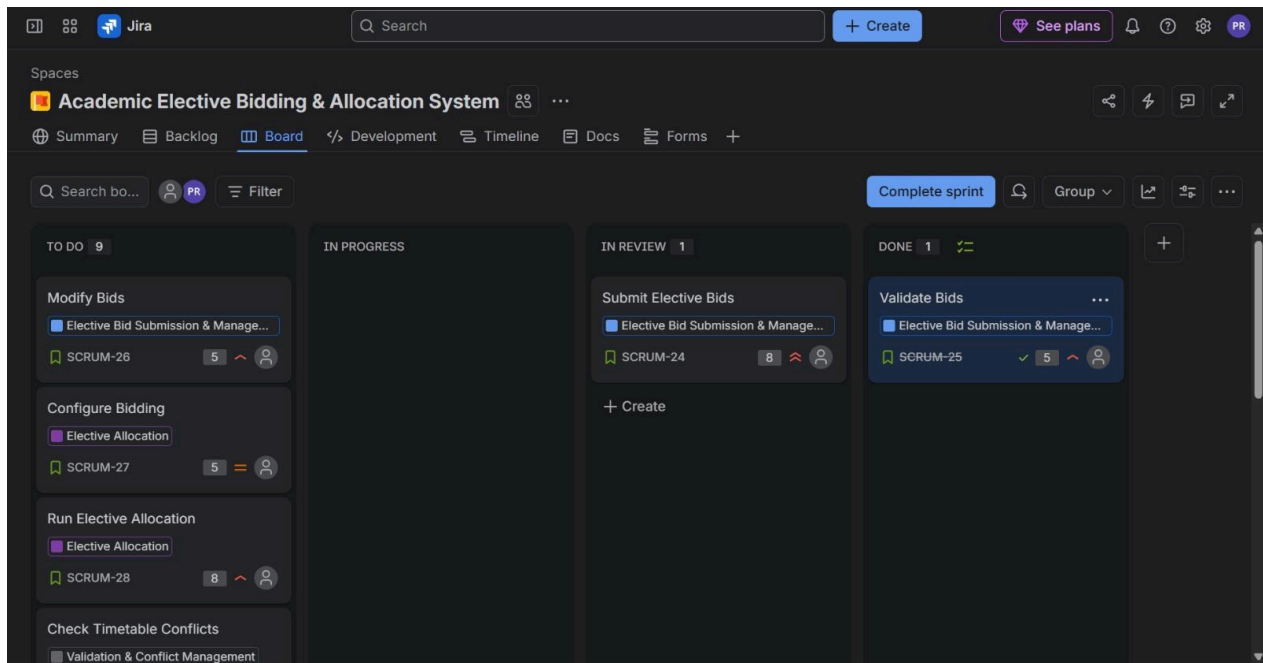


Figure 24. Sprint 2 board state with more work items completed.

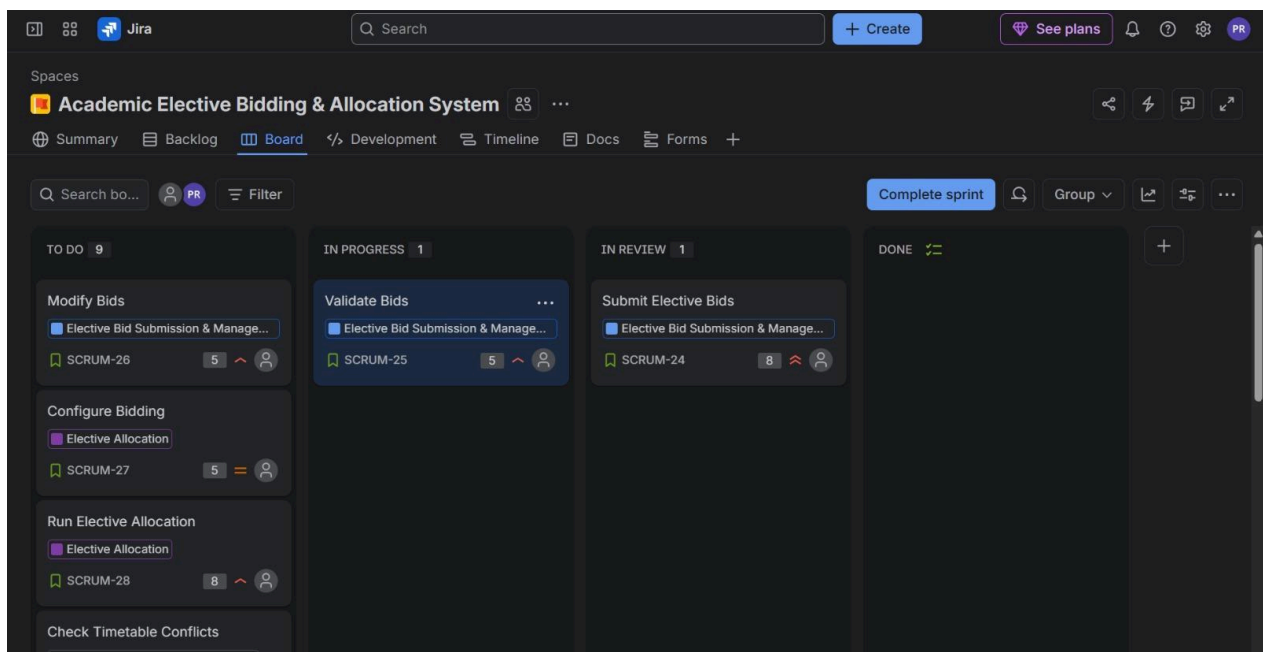


Figure 25. Sprint 2 board state showing the workflow nearing its final state.

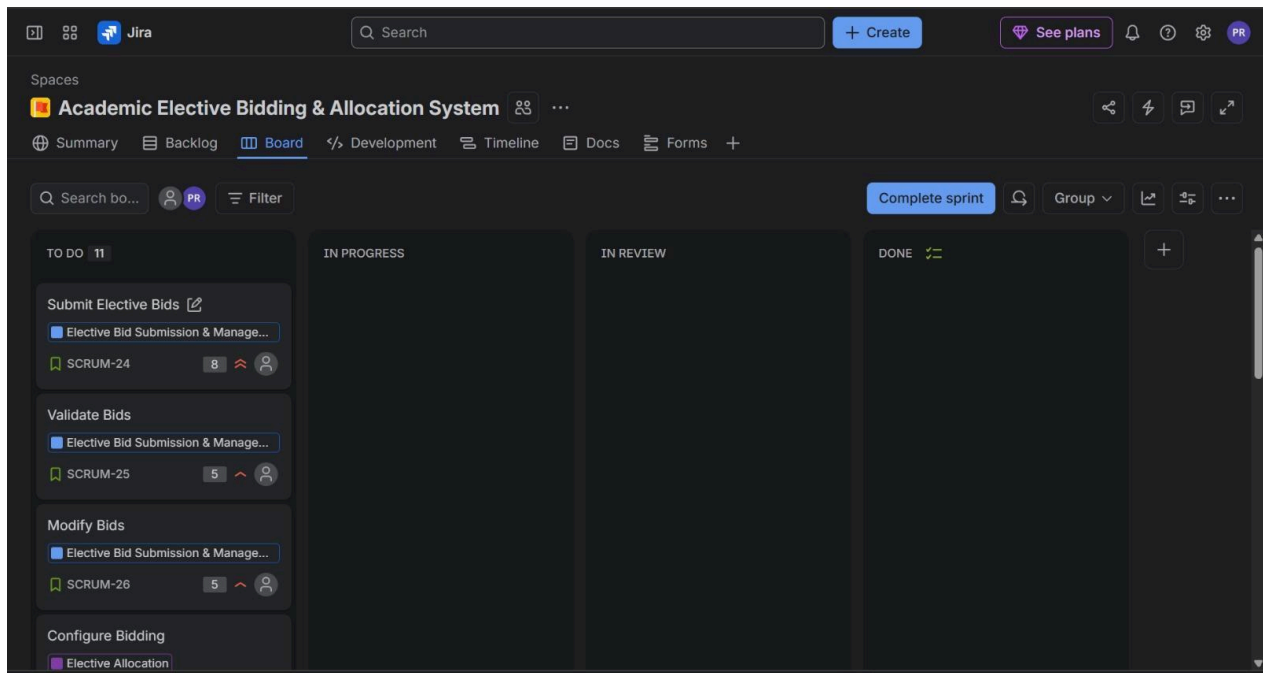
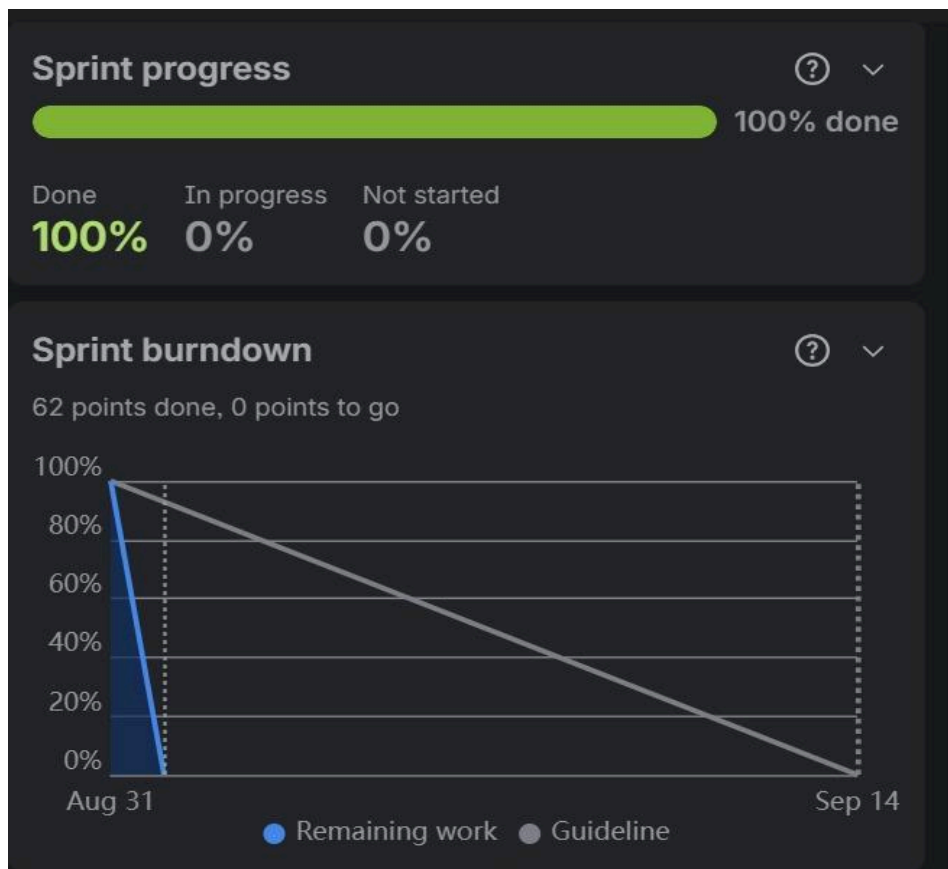


Figure 26. Sprint 2 board at the final execution stage before closure.

8.2 Sprint 2 Progress and Burndown

Sprint 2 carries the larger workload, with 62 story points across eleven stories. The final sprint tracker reports 100% done, and the burndown chart reaches zero remaining work.



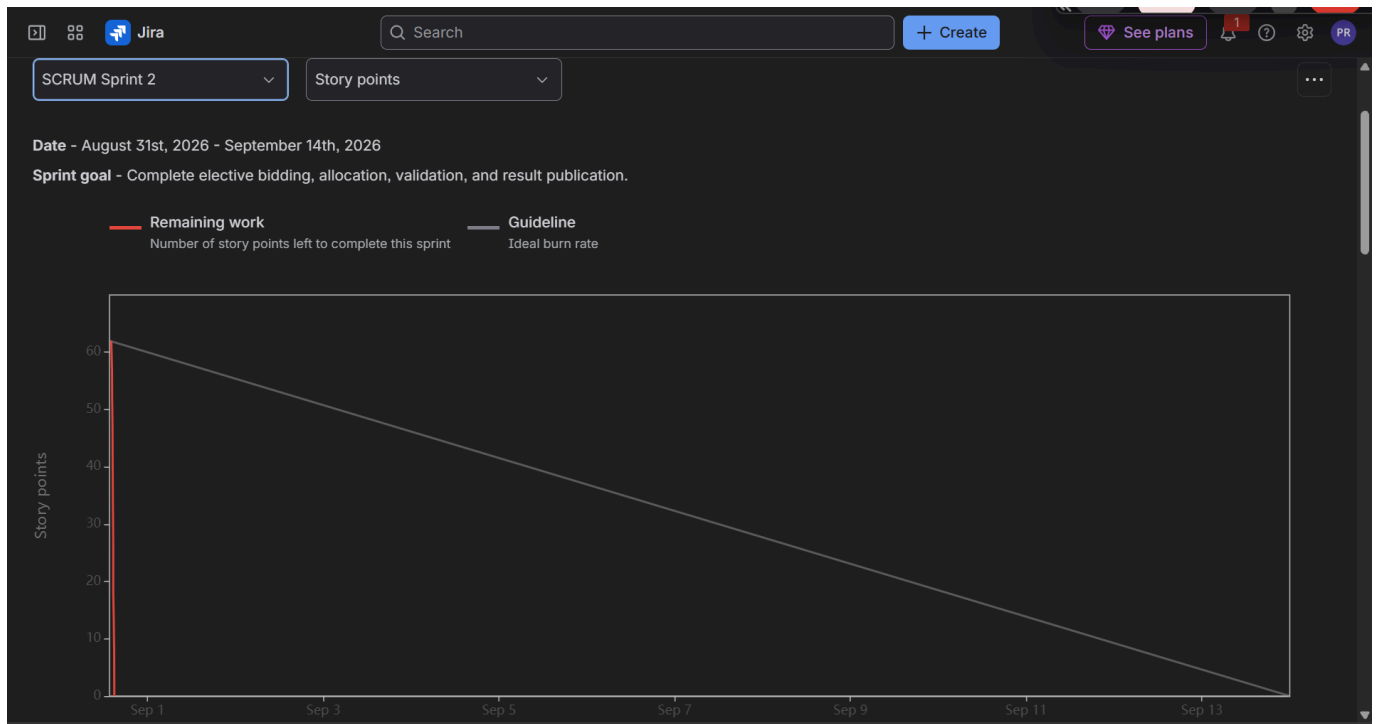


Figure 27. Sprint 2 sprint-progress tracker and burndown chart — 100% done, 0% in progress, 0% not started, with 62 points completed and 0 points to go.

9. Sprint Completion

9.1 Sprint 1 Completion

Sprint 1 was completed after all six committed work items reached Done. The completion evidence confirms the end of the sprint.




Figure 28. Sprint 1 completion confirmation — Jira reports 6 completed work items.

9.2 Sprint 2 Completion

Sprint 2 was completed after all eleven committed work items reached Done. The completion dialog provides the final confirmation.

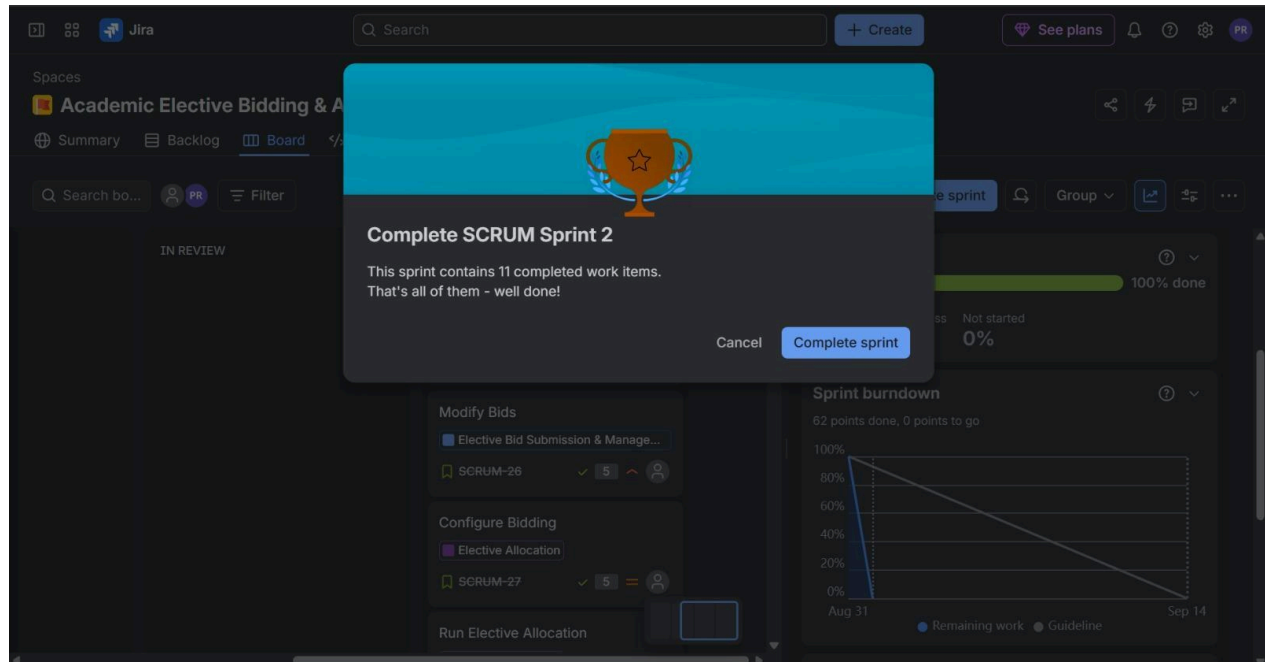


Figure 29. Sprint 2 completion confirmation — Jira reports 11 completed work items.

10. Sprint Summary

Metric	Sprint 1	Sprint 2
Primary focus	Student access, elective discovery and bidding credits	Bidding, allocation, validation, conflict handling and results
Committed stories	6	11
Story points	18	62
Final remaining points	0	0
Final status	Completed	Completed

The two sprints together cover the system from the student's initial access and preparation for bidding through bid processing, allocation, validation and publication of results.

11. Evidence Map

Evaluation Area	Evidence Included in This Report
Epics and User Stories	Epic tables, Epic Progress screenshots, backlog screenshots and master Epic/User Story table
Story Points and Priorities	Master planning table and Jira backlog screenshots
Sprint 1	Sprint 1 board, progress, burndown, activity/review and completion screenshots
Sprint 2	Sprint 2 board, progress, burndown, activity/review and completion screenshots
Comments / Review	Individual issue activity screenshot and In Review board evidence
Burndown Charts	Sprint 1 and Sprint 2 burndown screenshots
Sprint Completion	Sprint 1 and Sprint 2 completion dialogs

12. Conclusion

The Jira workspace provides a complete Agile Scrum record for the Academic Elective Bidding & Allocation System. The project is structured into six functional Epics and seventeen User Stories, with story points, priorities and sprint allocation recorded in the backlog. Sprint 1 delivers the student-access and bidding-credit foundation with 18 story points, while Sprint 2 delivers the main bidding, allocation, validation and results workflow with 62 story points. The board screenshots, comments, progress trackers, burndown charts and completion dialogs together provide evidence of the full Scrum workflow.

13. Report Structure Note

The layout of this report follows the useful structure demonstrated by the provided reference document: an Epic/User Story planning table with story points, priority and sprint allocation, followed by evidence sections for backlog planning, sprint execution, comments, burndown charts, sprint completion and summary. The content, project names, issue keys and screenshots in this report are specific to the Academic Elective Bidding & Allocation System rather than copied from the reference.
